MAREHOUSE

Electric Walkie Stacker Daily Checklist

DATE		INSPECTED BY	
MAKE	MODEL		S/N#
HOUR		VOLTAGE	

MARK BOX If NO PROBLEMS Visible. KEEP UNMARKED and WRITE IN Comment if PROBLEMS ARE PRESENT.

	ODED ATIONAL INSDECTIO
VISUAL INSPECTION Comments	OPERATIONAL INSPECTION
	A. Listen for Unusual Noise
1. Main ON/OFF Switch	B. Lifting Control
2.	C. Driving
3. Ly Key Switch	☐ Accelerator
4. Spec Plate Location	Steering
5. Directional/Speed Control	Braking
	D. Reverse Driving
6. Emergency Reverse Button	☐ Accelerators
7. Horn Button	Steering
8. Lift/Lower Button/Lever	Braking
9. Battery	Backup Alarm
U Vent Caps	E. Horn
Connector Covers	F. Gauges
☐ Cables	G. Oil Spots on Floor
Water Level	
10. Lift Cylinder	
11.	
12. Load Wheels	
13.	(6)
14. Caster Wheel	
	10-73
	(5) (5) (6)

SIGNATURE:






All comments made in reference to any problems should be made on the back of this page in detail and handed to the supervisor immediately.

CAUTION: This is not a complete list of all items which may require attention. Operators are responsible for ensuring that the lift truck is in proper working condition in accordance with the manufacturer's specifications.

DO NOT operate lift truck if a problem is detected.

Report all problems to the service department immediately.

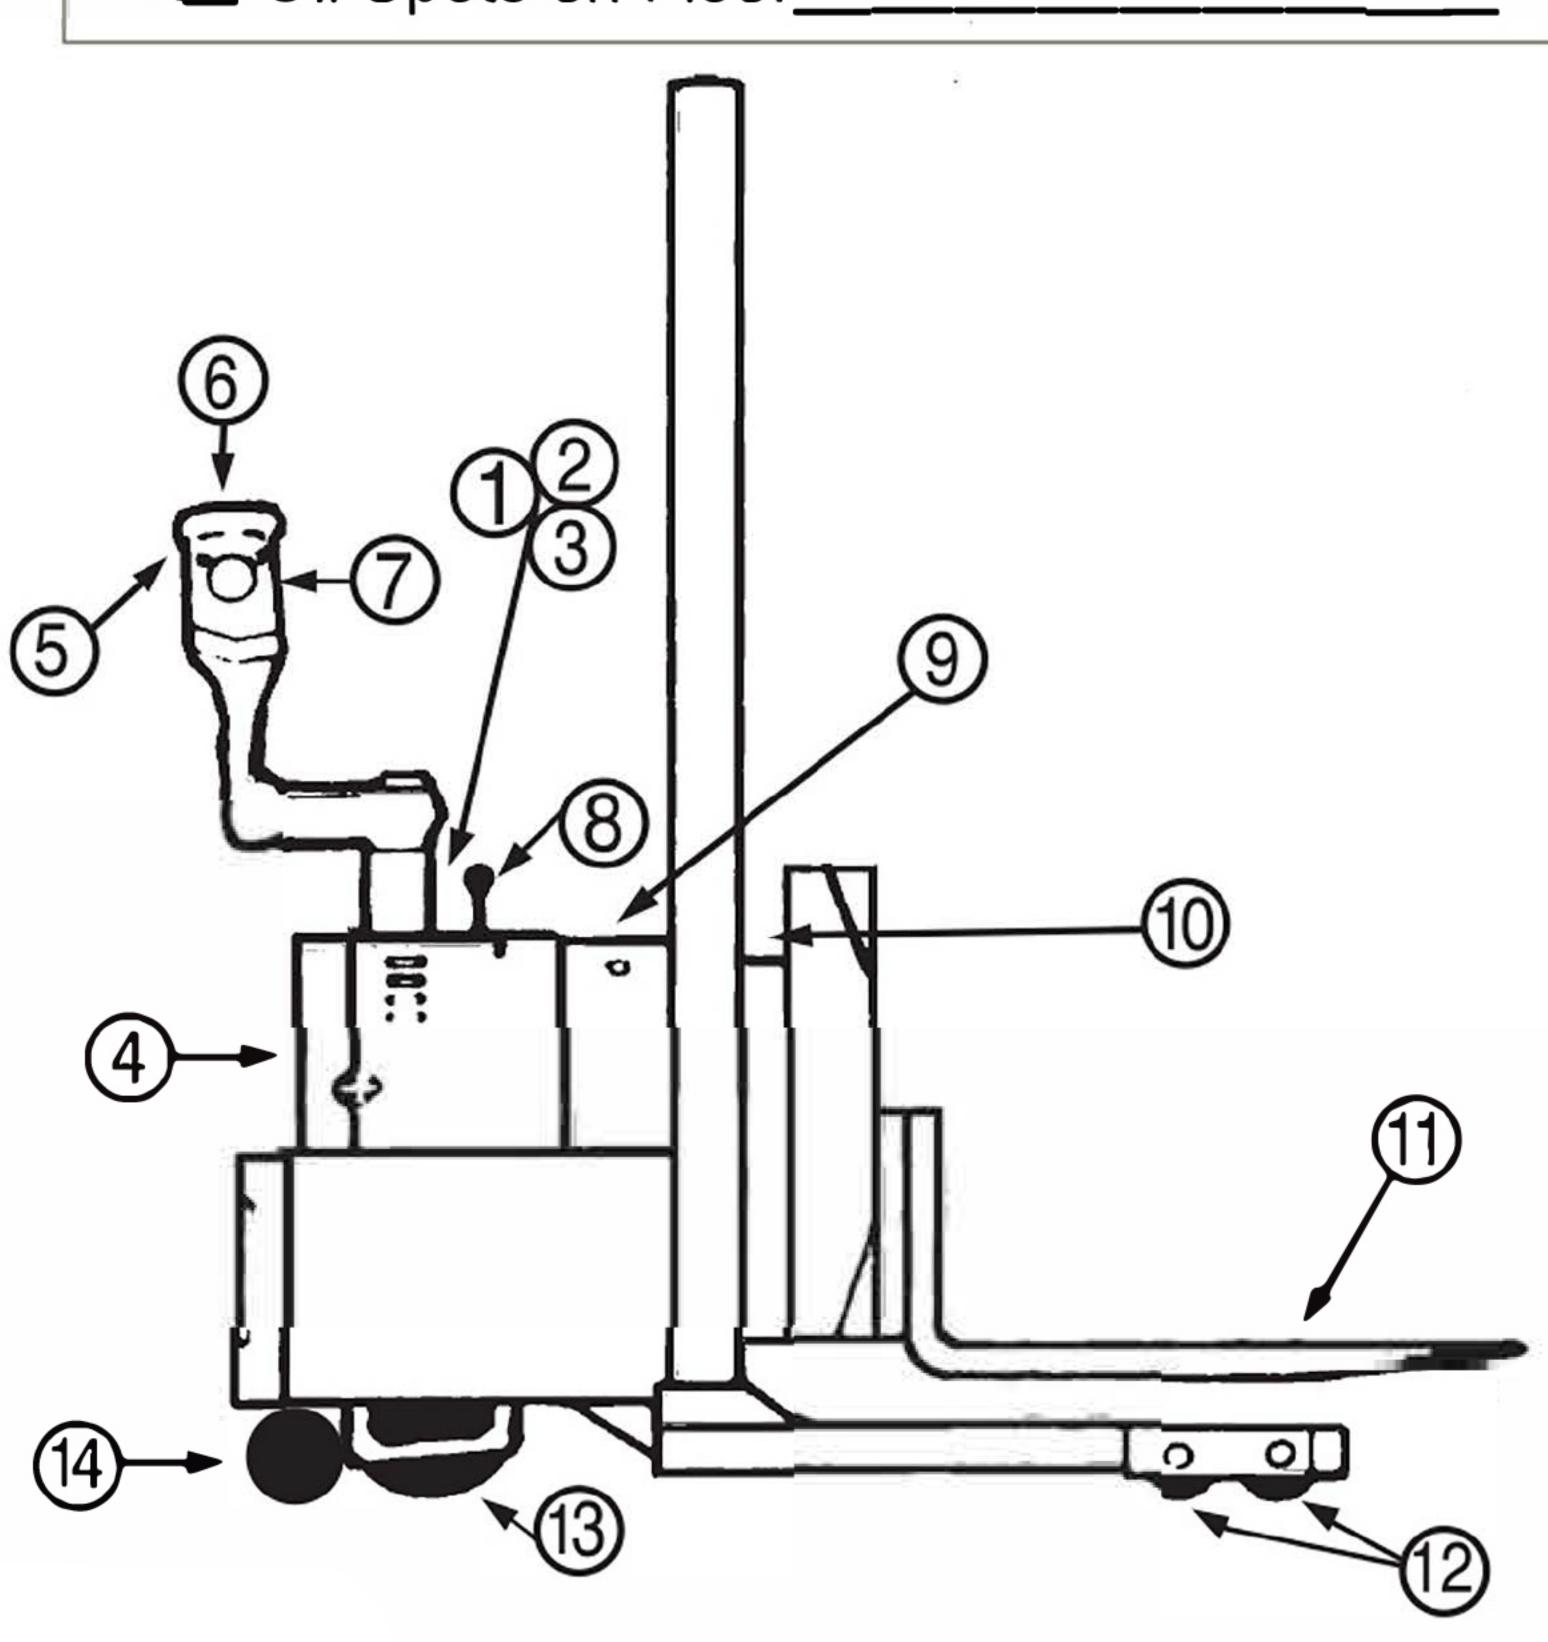

Comments
