

TOTAL WAREHOUSE

Electric Walkie Stacker Daily Checklist

DATE

INSPECTED BY

MAKE

MODEL

S/N#

HOUR

VOLTAGE

MARK BOX If NO PROBLEMS Visible. KEEP UNMARKED and WRITE IN Comment if PROBLEMS ARE PRESENT.

VISUAL INSPECTION

Comments


1. ☐ Main ON/OFF Switch_____
2. ☐ Hour Meter_____
3. ☐ Key Switch_____
4. ☐ Spec Plate Location_____
5. ☐ Directional/Speed Control_____
6. ☐ Emergency Reverse Button_____
7. ☐ Horn Button_____
8. ☐ Lift/Lower Button/Lever_____
9. ☐ Battery_____
- ☐ Vent Caps_____
- ☐ Connector Covers_____
- ☐ Cables_____
- ☐ Water Level_____
10. ☐ Lift Cylinder_____
11. ☐ Forks_____
12. ☐ Load Wheels_____
13. ☐ Drive Wheel_____
14. ☐ Caster Wheel_____

SIGNATURE: _____

OPERATIONAL INSPECTION

Comments

- A. ☐ Listen for Unusual Noise_____
- B. ☐ Lifting Control_____
- C. ☐ Forward Driving_____
- ☐ Accelerator_____
- ☐ Steering_____
- ☐ Braking_____
- D. ☐ Reverse Driving_____
- ☐ Accelerators_____
- ☐ Steering_____
- ☐ Braking_____
- ☐ Backup Alarm_____
- E. ☐ Horn_____
- F. ☐ Gauges_____
- G. ☐ Oil Spots on Floor_____

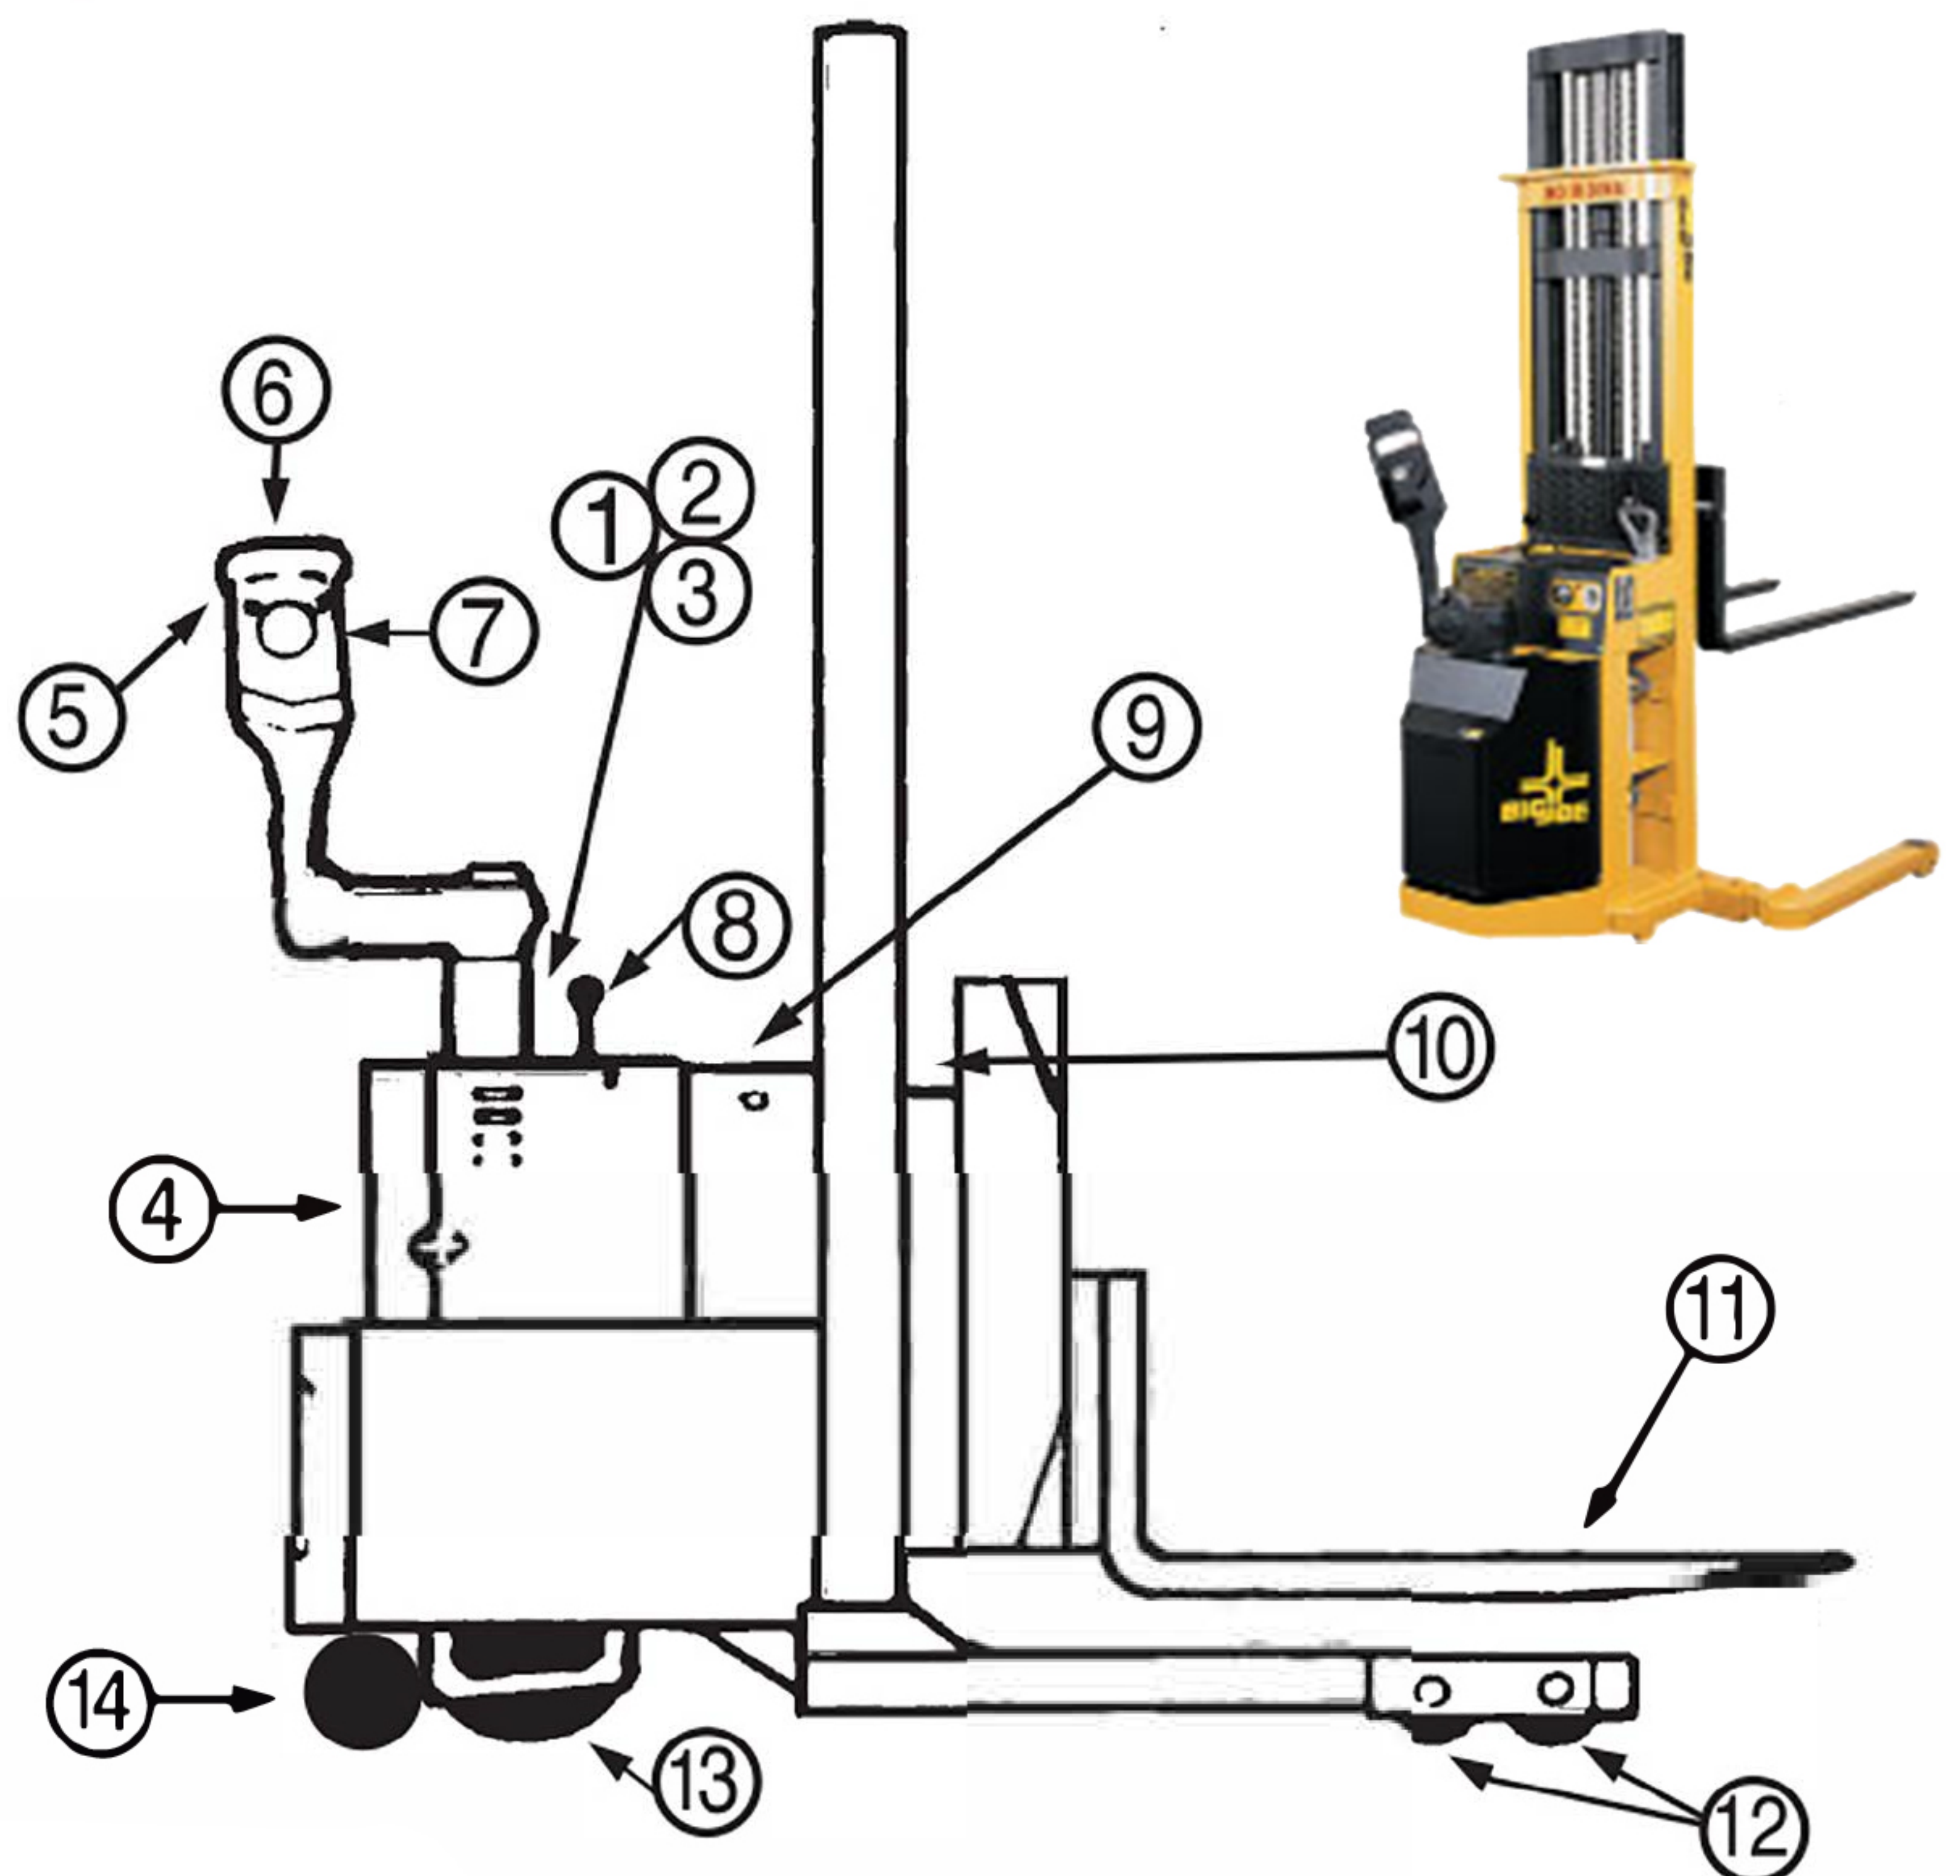

All comments made in reference to any problems should be made on the back of this page in detail and handed to the supervisor immediately.

CAUTION: This is not a complete list of all items which may require attention. Operators are responsible for ensuring that the lift truck is in proper working condition in accordance with the manufacturer's specifications.

DO NOT operate lift truck if a problem is detected.
Report all problems to the service department immediately.
